



Weekly Project Updates and 7-Day Look-Ahead

# Here is a look-ahead at the construction work planned for the Public Safety Building, from July 26, 2021 to July 30, 2021

## **Project Overview:**

Construction of a combined public safety building commenced in December 2020 on the site of the former Town Hall at 26 Bryant Street. The new building will house the staff and equipment of Fire, Police, and Dispatch departments. The new combined Public Safety Building will replace two older Town buildings: Police Station at 600 High Street (built in 1962) and the Fire Station at 436 Washington Street (built in 1930). The new building is scheduled to open in the Fall of 2022.

The <u>livestream video</u> of the construction is now available on the Project website! Tune in from anywhere to watch the continued progress on the Combined Public Safety Building.

## What to expect July 26, 2021 (Monday) through July 30, 2021 (Friday):

- The project site remains closed to the public.
- Crews will be working onsite on **Saturday**, **July 24**, **2021**, **from 8:00 AM to 4:00 PM** for welding and detailing, and to perform overall site clean-up/consolidation.
- The project team and construction crews have made tremendous progress installing the structural steel onsite. Steel installation will continue next week using the crane located onsite.
- To maintain an efficient and organized jobsite, crews will continue to remove excess material for the site.
- Deliveries of steel and metal decking will continue next week.
- The dewatering system remains in place and operational.
- Next week, crews will continue to install waterproofing and damp proofing at the foundation walls.
- Localized anchor and foundation repairs are on-going.
- Expect periodic entrance and exit of large trucks at the project site entrance, located at the intersection of Washington Street and Bryant Street. Please expect minor traffic delays at this intersection.
- No additional traffic impacts or pedestrian impacts are anticipated during this week.

### **Construction Hours:**


- Crews will be working onsite on **Saturday**, **July 24 from 8:00 AM to 4:00 PM**. Trucks may be entering and exiting the site to remove material.
- Crews will be onsite next week, Monday through Friday, from 7:00 AM to 5:00 PM

### **Project Team Contact Information:**

- Immediate issues or concerns, please contact the Dedham Town Manager's Office at 781-751-9100.
- For general questions or concerns, please contact the project team at <u>psb@dedham-ma.gov</u>
- For more information about the Public Safety Building Project, please visit the project website at <a href="https://www.dedham-ma.gov/psb">www.dedham-ma.gov/psb</a>
- Download our project team contact information flyer on the project website.



**Caption:** Photo taken from ground level of the project site facing Stairwell #1, looking south.

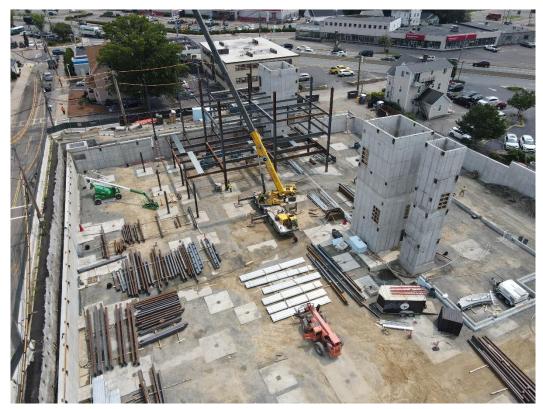

**Caption:** Aerial photo of construction site on July 21, 2021. A crane is used to raise and place each piece of steel, one a time, for installation by onsite crew members. Pieces of steel are being delivered to the site and securely stored along the west and south walls, shown at the left of this photo.

**Note:** To subscribe to the Public Safety Building Project e-mail notifications, <u>click here</u> to provide your name and email address.
