



PUBLIC SAFETY BUILDING PROJECT



Weekly Project Updates and
7-Day Look-Ahead

**Here is a look-ahead at the construction work planned for the Public Safety Building,
from January 10, 2022 to January 14, 2022**

Project Overview:

Construction of a combined public safety building commenced in December 2020 on the site of the former Town Hall at 26 Bryant Street. The new building will house the staff and equipment of Fire, Police, and Dispatch departments. The new combined Public Safety Building will replace two older Town buildings: Police Station at 600 High Street (built in 1962) and the Fire Station at 436 Washington Street (built in 1930). The new building is scheduled to open in the Fall of 2022.

A [livestream video](#) of the construction is available on the Project website! Tune in from anywhere to watch the continued progress on the Combined Public Safety Building. While there, check out the updated Before-and-After photos of the progress onsite.

What to expect January 10, 2022 (Monday) through January 14, 2022 (Friday):

- The project site remains closed to the public.
- Dewatering system is still operational and the site contractors are backfilling the underground telecommunications and data duct banks along the west and south sides of the site.
- Crews will be working onsite **Saturday, January 8, 2022 and Sunday, January 9, 2022**, to remove snow and to continue to spray fireproofing in the garage. Snow will be removed from the site, so trucks will be entering and exiting from the corner of Washington Street and Bryant Street. Please use caution in this area.
- As of **Friday, January 7, 2022**, Eversource has installed four out of five new utility poles along Bryant Street at the western side of the site.
- On **Monday, January 10, 2022**, crews will continue to run the rough electrical through the concrete masonry unit (CMU) walls in the garage. Within the garage, crews will all continue to install 4" CMU walls,
- Roofers will begin installing the roof framing and parapet walls at the edges of the roof.
- Crews will continue to install spray fireproofing materials in the basement to protect structural elements from extreme temperatures and heat generated by fire.
- The installation of interior and exterior cold form metal framing and Densglass sheathing will continue this week.
- Expect periodic entrance and exit of large trucks at the project site entrance, located at the intersection of Washington Street and Bryant Street. **Please expect minor traffic delays at this intersection.**
- No additional traffic impacts or pedestrian impacts are anticipated during this week.

Public Viewing Area:

If you want to stop by to check out the progress, stand by the picnic table outside the north entrance to Town Hall. This spot provides a great view into the project site and is outside of the project boundaries. Worth a visit!

Construction Hours:


- Crews will be onsite:

- Monday through Friday: 7:00 AM to 5:00 PM
- Saturday, January 8, 2022 from 8:00 AM to 4:00 PM
- Sunday, January 9, 2022 from 8:00 AM to Noon

Project Team Contact Information:

- Immediate issues or concerns, please contact the Town Manager's Office at [781-751-9100](tel:781-751-9100).
- For general questions or concerns, please contact the project team at psb@dedham-ma.gov
- For more information about the Public Safety Building Project, please visit the project website at www.dedham-ma.gov/psb
- Download our [project team contact information flyer](#) on the project website.

Click on the image below to enlarge

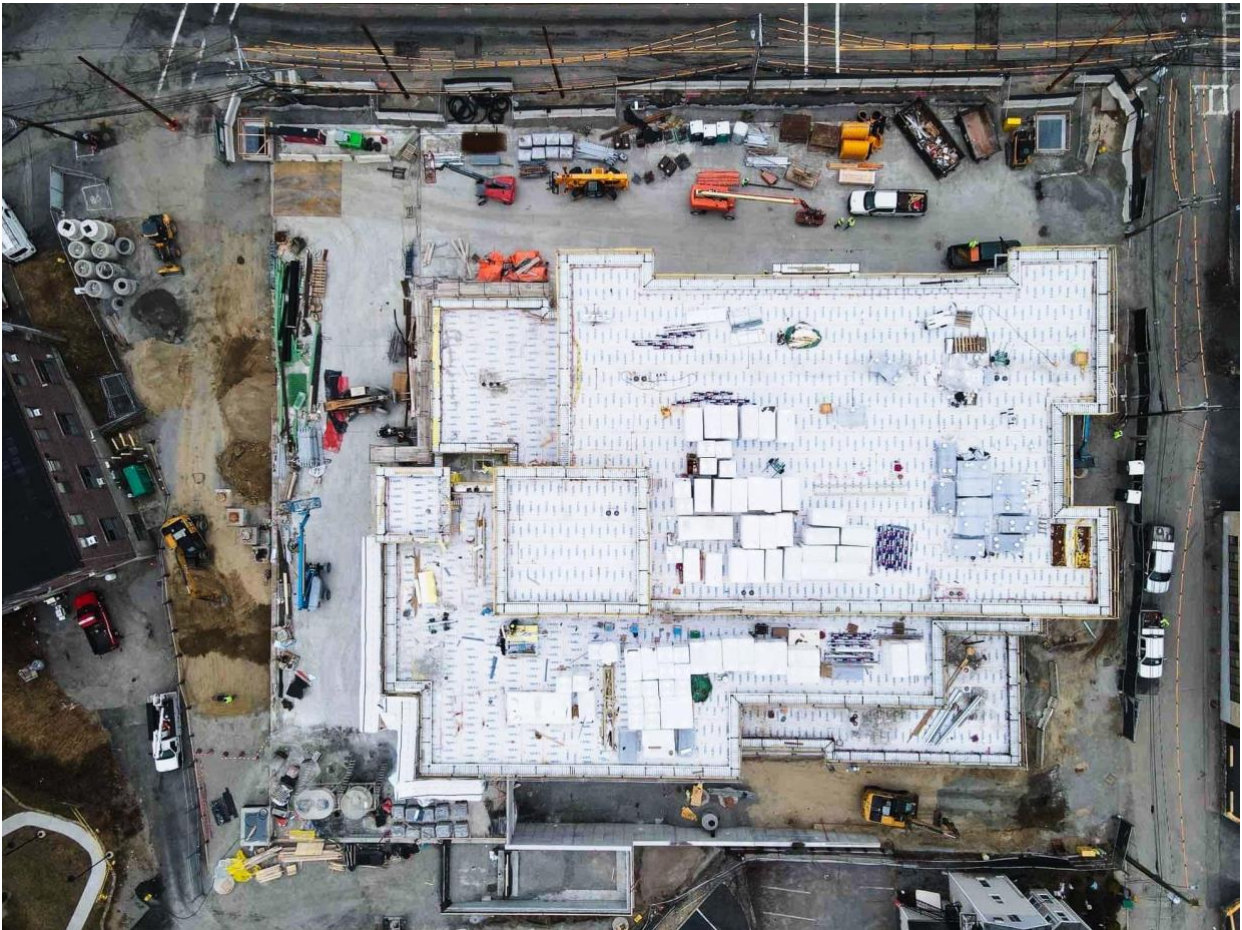

Caption: Aerial photo of the active construction site taken by Commodore Builders, with Bryant Street at the top of the photo and Town Hall to the left. Roofing and parapet wall materials are shown stacked on the roof awaiting installation. The generator pad at the bottom of the photo has been backfilled and covered with a concrete pad.

Note: To subscribe to the Public Safety Building Project e-mail notifications, [click here](#) to provide your name and email address.
